



PUBLIC WORKS




○ ○ ○ ○

CAPITAL IMPROVEMENT PROJECTS

NEWSLETTER

MONDAY

JUNE 2, 2025

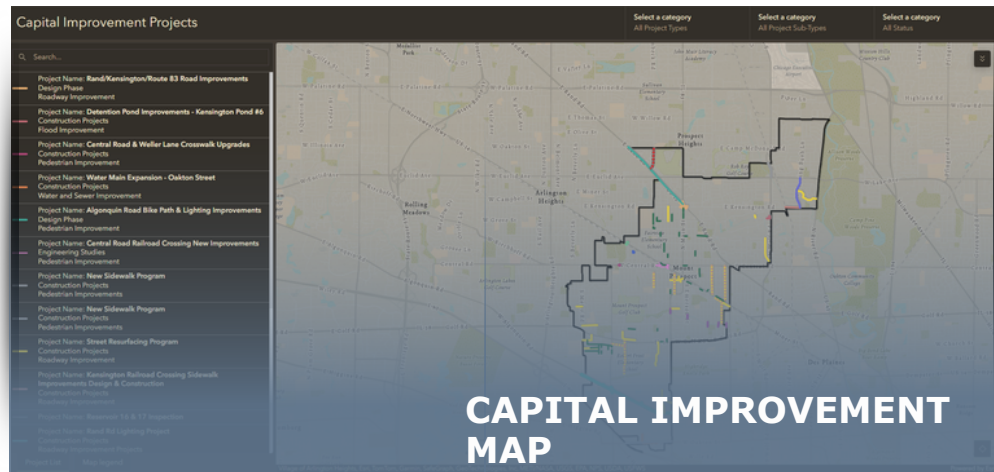

CAPITAL IMPROVEMENT MAP

Mount Prospect Public Works: Infrastructure at Your Fingertips

Ever wonder what's happening beneath your feet or just around the corner? Our Village Infrastructure Projects page is your go-to source for all things Public Works. From road resurfacing to sewer upgrades, we're putting the spotlight on the projects that keep our village running smoothly.

But wait, there's more! We've launched an interactive project map that puts the power of information at your fingertips. Click around to explore current, upcoming, and recently completed infrastructure projects throughout Mount Prospect. Whether there's construction near your morning coffee stop or sidewalk upgrades by your favorite park, you'll know what's happening—and why. Click on any project to get details, timelines, and understand how it might impact your daily routine. It's transparency and community engagement, all in one place.

<https://www.mountprospect.org/departments/public-works/village-infrastructure-projects>



Water Main Project

This year's Water Main Improvement Project is a cornerstone of our commitment to modernizing essential infrastructure. This initiative involves replacing over 15,000 linear feet of aging water mains, along with associated fire hydrants, valves, and residential service lines. The project targets areas with a history of frequent water main breaks, aiming to enhance water flow, pressure, and overall system reliability. The contractor is continuing to transfer water services from the old main to the new water main on Louis Street. This also entails full water service line replacements for properties that have lead water service lines. The landscape restoration contractor will continue to work on Albert Street installing sod. Additionally, this week, the contractor will deliver materials to Can Dota Ave in preparation for work to begin there on June 9th.



<https://www.mountprospect.org/departments/public-works/village-infrastructure-projects/water-main-improvements>



Resurfacing Program

The 2025 Street Resurfacing Program will repave 6.8 miles of our 137-mile roadway network, focusing on both surface improvements and underlying infrastructure. Group 1 covers 3.3 miles of standalone resurfacing, while Group 2 integrates with the Water Main Improvement Project to address 3.5 miles of road. In addition to new asphalt, the work includes repairing storm inlets, replacing deteriorated curbs and sidewalks, and restoring parkways. Over the next few weeks, the contractor will be out in the field removing and replacing damaged sidewalk, curbs, and drainage structures at Pine Street (Lincoln to Prospect Ave), Evergreen Ave (Elmhurst Ave to Main St), Albert St (Northwest Highway to Central Rd), and Lonquist Blvd (Meier Rd to Crestwood Ln). Once the concrete improvements are complete, crews will proceed to pavement grinding and roadway resurfacing to finalize the upgrades.



<https://www.mountprospect.org/departments/public-works/village-infrastructure-projects/combined-sewer-improvements>

Sanitary & Storm Sewer Lining

The 2025 Sanitary Sewer Lining Project is a key initiative aimed at enhancing the durability and efficiency of our sewer infrastructure. Utilizing the



cured-in-place pipe (CIPP) method, this trenchless technology allows us to rehabilitate aging sewer lines by inserting a new liner within the existing pipes, minimizing excavation and disruption to the community. The contractor has completed the preparation phase for the Combined and Separate sanitary sewer lining project. They are currently working on the preparation phase for the storm sewer lining segments, which entails televising the sewers to find obstructions before lining. The preparation phase should be 100% completed by the week of June 9th, with the lining phase beginning immediately afterwards.

<https://www.mountprospect.org/departments/public-works/village-infrastructure-projects/combined-sewer-improvements>

Arterial Bike Network Study

Mount Prospect, in partnership with Civiltech Engineering, completed the Arterial Bike Network Study to map out safer, more connected bike routes along our busiest roads. Funded in part by an IDOT grant, the study doesn't just guide future projects—it gives us an edge when applying for more grant funding. Next up, the Village will begin targeting the highest-priority routes identified in the plan. Phase I Engineering has already been budgeted, but we haven't started the RFP process yet. Public Works plans to initiate a project before the end of the year to keep things moving forward. It's all part of our effort to make biking a safer and easier option for getting around town. Big picture: we're building smarter, more sustainable streets—one project at a time.



<https://www.mountprospect.org/departments/public-works/engineering/traffic/arterial-bike-network-study>

